TABULATION OF SIGNS AND DEVICES FOR DETOUR ROUTE MAINTENANCE AND PROTECTION OF TRAFFIC DURING CONSTRUCTION

NO.	LEGEND	NOMENCLATURE	SIZE	MOUNTING	QUANTITY	REMARKS
1	DETOUR	M4-9L	30"X24"	TYPE B	3	
2	DETOUR	M4-9SL	30"X24"	TYPE B	3	
3	ROAD CLOSED 1000 FT	W20-3 W30-1-2	36"X36" 20"X6"	TYPE B	1	
4	BRIDGE CLOSED	R11-2-1	48"X30"	TYPE III BARRICADE	2	BARRICADES MUST EXTEND ACROSS FULL WIDTH OF TWIN ARCH RD. PLACE ADJACENT TO PRIVATE ACCESS GATE. DO NOT BLOCK GATE.
5	ROAD CLOSED 500 FT	W20-3 W30-1-1	36"X36" 20"X6"	TYPE B	1	
6	BRIDGE OUT  1 MILE AHEAD  LOCAL TRAFFIC ONLY  DETOUR	R11-3B R11-3A M4-10L	48"X12" 60"X30" 48"X18"	TYPE III BARRICADE	2	PLACE ON LEFT AND RIGHT SIDES OF TWIN ARCH ROAD AT INTERSECTION OF TUNNEL HILL ROAD.
7	END DETOUR	M4-8A	24"X18"	TYPE B	2	
8	DETOUR	M4-9R	30"X24"	TYPE B	4	
9	DETOUR	M4-9SR	30"X24"	TYPE B	4	
<b>*</b> 10	THIS BRIDGE TO BE CLOSED FOR CONSTRUCTION < DATE >	W23-101	96"X48"	TYPE III BARRICADE	2	PLACE ON RIGHT SIDE OF TWIN ARCH ROAD.
11	BRIDGE CLOSED DETOUR	R11-2-1 M4-10R	48"X30" 48"X18"	TYPE III BARRICADE	_	BARRICADES MUST EXTEND ACROSS FULL WIDTH OF TWIN ARCH ROAD AT INTERSECTION OF REYNOLDS MILL ROAD.
12	DETOUR	M4-9-1BL	30"X24"	TYPE B	1	
13	DETOUR	M4-9-1AL	30"X24"	TYPE B	1	
14	DETOUR	M4-9-1AR	30"X24"	TYPE B	1	

<sup>\*</sup> TO BE INSTALLED TWO (2) WEEKS PRIOR TO IMPLEMENTING THE DETOUR AND REMOVED ONCE DETOUR IS IN PLACE.

DISTRICT	COUNTY	ROUTE	SECTION	SHEET				
8-0	YORK	– BRG		1 OF 1				
NORTH CODORUS, SPRINGFIELD, AND YORK TOWNSHIP								
REVISION NUMBER	REVISION	DATE	BY					

## **GENERAL NOTES**

DETOUR IS IN ACCORDANCE WITH PATA 216 OF PUBLICATION

FURNISH, ERECT, PLACE AND MAINTAIN TRAFFIC CONTROL SIGNS AND DEVICES. MAINTAIN TRAFFIC DURING HOURS OF CONSTRUCTION AND AT ALL OTHER TIMES IN ACCORDANCE WITH THE METHODS INDICATED ON THESE DRAWINGS AND THE FOLLOWING:


- 1. THE SPECIAL PROVISIONS OF THE CONTRACT.
- 2. THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES
- 3. PENNDOT PUBLICATION 212, OFFICIAL TRAFFIC CONTROL
- DEVICES, SUBCHAPTER E.
  4. PENNDOT PUBLICATION 213, TEMPORARY TRAFFIC CONTROL
- 5. PENNDOT PUBLICATION 35, APPROVED CONSTRUCTION
- MATERIALS (BULLETIN 15).

  6. PENNDOT PUBLICATION 408, SPECIFICATIONS.
- 7. PENNDOT PUBLICATION 111, TRAFFIC CONTROL PAVEMENT MARKINGS AND SIGNING STANDARDS, TC-8600 AND TC-8700 SERIES.
- 8. PENNDOT PUBLICATION 236 HANDBOOK OF APPROVED SIGNS.

CONTRACTOR SHALL COOPERATE AND COORDINATE WITH ANY ADJACENT CONTRACTOR IN THE MAINTENANCE AND PROTECTION OF TRAFFIC DURING CONSTRUCTION. COORDINATE THE PLACEMENT, COVERING, AND/OR REMOVAL OF SIGNS AND TRAFFIC CONTROL DEVICES THROUGHOUT THE DURATION OF THIS CONTRACT.

DETOUR WILL LAST APPROXIMATELY 120 CALENDAR DAYS.



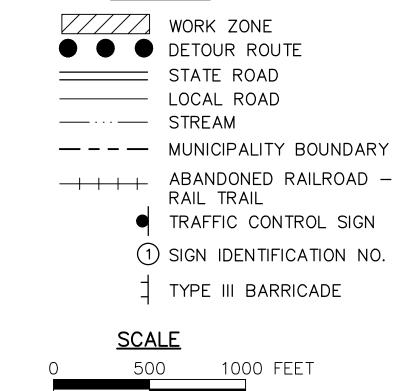

HERBERT, ROWLAND & GRUBIC, INC.
369 EAST PARK DRIVE
HARRISBURG, PA 17111

DETOUR LENGTH = 3.3 MILES

YORK COUNTY BRIDGE NO. 89 - TWIN ARCH ROAD (T-502/T-504) TRAFFIC CONTROL PLAN

11/10/2020
